DETOUR MAP
CARROLL AVENUE BRIDGE PROJECT

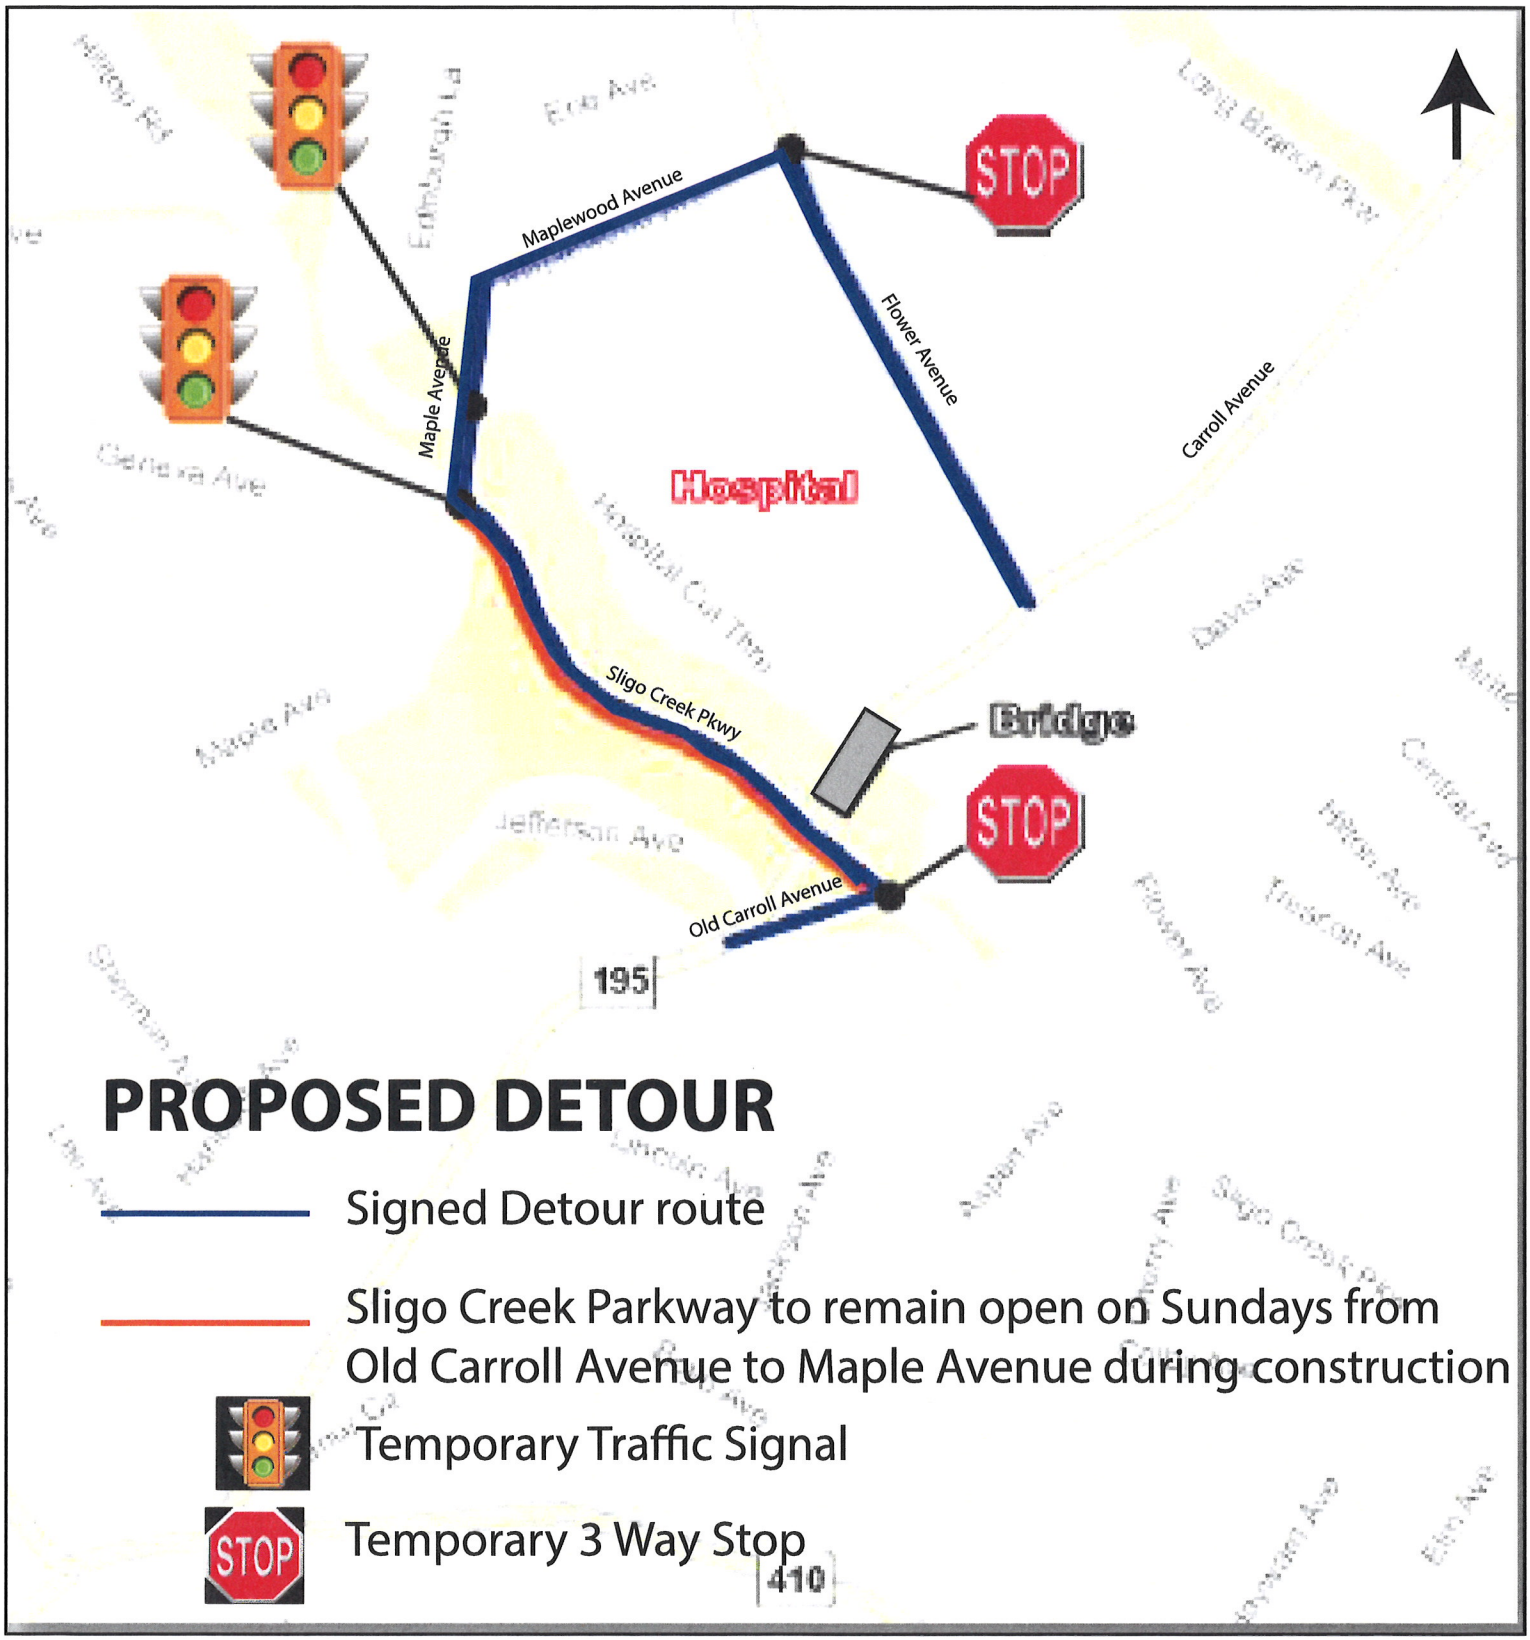

RECOMMENDED TRAFFIC CALMING MEASURES

		IMPLEMENTING AGENCY	ADD'L COMMENTS *(italics indicate changed since Sept 8th Council Presentation)*
CROSSWALKS/PEDESTRIAN CROSSING SIGNS			
Carroll Avenue	crosswalks at Boyd & Lincoln	SHA	District 3 office agreed to install crosswalk at Boyd, though it is not part of this project, District 3 office evaluating at Lincoln
Maplewood Ave	pedestrian crossing signs at Maple and Flower	TP	*revised*
Maple Avenue	crosswalk markings at Grant, Lee, Sherman, Ritchie, Lincoln to be refurbished *	TP	Received Safe Routes To School grant for this project, working through approvals to implement prior to bridge closure
Maple Avenue	pedestrian crossing signs at intersections along detour route	TP	*to be located at each intersection between Lee and Lincoln*
Old Carroll Avenue	crosswalk at Carroll Avenue (to be installed by SHA contractor)	SHA	Agreed to by SHA , will be installed as part of project
NEW SIDEWALK			
Sligo Creek Parkway	sidewalk between Old Carroll and Jackson	MNCPPC, TP	Agreed to by MNCPPC - they are completing design, to be installed by City contractor at City's expense
ONE WAY / NO ENTRY / TURN RESTRICTIONS			
Jefferson Avenue	no entry at Carroll & Jefferson	TP	
PARKING RESTRICTION			
Grant Avenue	extend No Parking area further up Grant from Maple	TP	*Addition, extend no parking area 100 feet from corner*
Maple Avenue	restrict parking on even side of 7500 block of Maple for morning rush hour		*Addition, recommend restriction from 7:30 to 9:30*
Maplewood Avenue	extend no parking area (north side) to enable bus turns from Flower Ave	TP	
Maplewood Avenue	no parking on college side (odd side)	TP	
Old Carroll Avenue	no parking on both sides of street	TP	
SIGNAGE / PAINTING			
Carroll Avenue	advanced variable message boards on either side of approach to bridge	SHA	
Carroll Avenue	detour ahead signs starting at 1,500 feet prior to bridge (before Garland Ave)	SHA	
Edinburgh Lane	Install signage - No access to SCP at Maple Edinburgh intersection	TP	
Flower Avenue	detour ahead signs north bound at Jackson	TP	
Flower Avenue	detour ahead signs southbound at Houston	TP	
Maple Avenue at Maplewood	install stop sign on Maple	TP	*addition*
Maplewood Avenue	paint center line	TP	
Sligo Creek Parkway	stop ahead & detour ahead signs north bound and south bound	MNCPPC, SHA	
TRAFFIC SIGNAL ISSUES			
Takoma Junction	Improve signal timing	SHA	
OTHER MEASURES		**Authority**	
Monitor traffic for 3 days on each impacted street prior to closure to establish pre-construction baseline		TP	To be completed in mid-September by City contractor - a total of 15 street segments will receive traffic counts*
Encourage "kind driving" through Newsletter articles and social media		TP	
Require contractors staff to park within construction zone, not on residential streets		SHA	Contractor is required to observe all local parking regulations, sufficient room for parking within construction zone.
Actively advertise Ride Share resources		TP	
Paint all crosswalks and stop bars in area prior to bridge work		TP	
Snow removal for detour routes needs to be high priority		SHA, MNCPPC, TP	

List of Streets for traffic count - Original List

1. Lincoln Avenue (between MD 195 (Carroll Avenue) and Maple Avenue)
2. Lincoln Avenue (between Jackson Avenue and Boyd Avenue)
3. Sherman Avenue (between Hancock Avenue and Maple Avenue)
4. Grant Avenue (between Hancock Avenue and Maple Avenue)
5. Lee Avenue (between Hancock Avenue and Maple Avenue)
6. Maple Avenue (between Lincoln and Sligo Creek Parkway)
7. Maple Avenue (between Sligo Creek Parkway and Maplewood)
8. Maplewood Avenue (between Maple Avenue and Flower Avenue)
9. Erie Avenue (between Maple Avenue and Flower Avenue)
10. Boyd Avenue (between Lincoln Avenue and Jackson Avenue)

*** Additional List**

11. Erie Avenue (between Flower and Maple)
12. Kennebec Avenue (between Flower and Maple)
13. Flower Avenue (between Carroll and Jackson)
14. Central Avenue (between Carroll and Jackson)
15. Garland Avenue (between Carroll and Jackson)
